


**PROJECT DESCRIPTION**  
 The Florida PALM project is replacing the Florida Accounting Information Resource Subsystem (FLAIR) and the Cash Management Subsystem (CMS) with a core Enterprise Resource Planning (ERP) solution. The project has completed the Pre-Design, Development and Implementation (Pre-DDI) phase which consisted of four tracks: Business Process Standardization (BPS), Project Management Office (PMO) including procurements, Organizational Change Management (OCM) including Workforce Transition (WFT), and System and Data Strategy (SDS). The project has executed a contract with a Software and Systems Integrator (SSI) as of July 20, 2018. The team has transitioned to the DDI phase of the project.

<b>SCHEDULE DATA</b>		<b>COST DATA   FY 2021-22</b>		
<b>Start Date</b> May 19, 2014	<b>Original Finish Date <sup>1</sup></b> August 26, 2026	<b>Appropriated Budget <sup>4</sup></b> \$35,730,837	<b>Planned Project Budget</b> \$32,235,786	<b>Actual Expenditures to Date</b> \$9,915,905
<b>Planned Finish Date <sup>2</sup></b> June 30, 2027	<b>Forecasted Finish Date <sup>3</sup></b> May 20, 2026	<b>Total Estimated Project Cost</b> \$286,905,137		
<b>Schedule / Cost Data Notes</b>				
<sup>1</sup> Original Finish Date is the date the project was originally forecasted to end based on the October 2018 DDI Project Schedule, which was one of the first schedules developed in collaboration with the vendor. This date does not include Production Support, which continues through June 30, 2027. <sup>2</sup> Planned Finish Date is the project end date listed in the Monthly Status Report from the current reporting period. <sup>3</sup> Forecasted Finish Date is the project end date reported in the DDI Project Schedule from the current reporting period. This date does not include Production Support, which continues through June 30, 2027. <sup>4</sup> Appropriated Budget is listed in the Monthly Status Report from the current reporting period.				

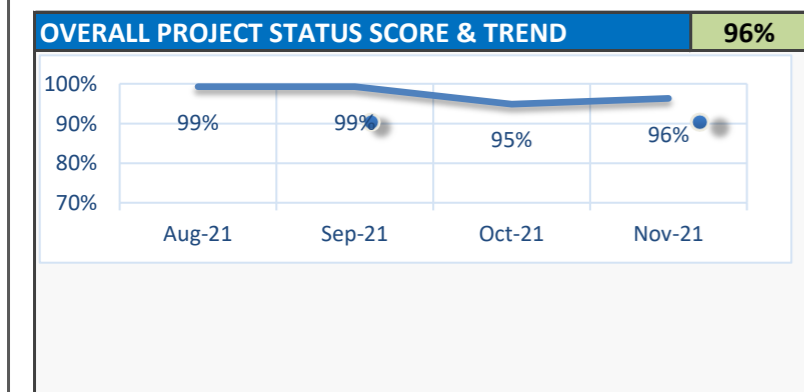

**KPI SCORING LEGEND**

<b>0 - 71.99%</b>	High Risk	May require escalation
<b>72 - 85.99%</b>	Medium Risk	Needs attention
<b>86 - 100%</b>	Low Risk	Monitor and maintain; continuous process improvement

**NOTES REGARDING OVERALL PROJECT STATUS**  
 According to the current spend plan and schedule, the Florida PALM Project is currently within budget for the fiscal year, and the schedule is forecasted to finish on time.

**SCOPE MANAGEMENT** **100%**  
 Scope Management presents low risk.  
 According to the Monthly Status Report, there was one approved change request in the reporting period.  
 PCR 83 removed the baselined dates for the tasks associated with a deliverable. There is a moderate impact to the schedule; however, the overall project end date is not changed. There is no impact to scope or budget.

**SCHEDULE MANAGEMENT** **75%**  
 Schedule Management presents medium risk.  
 For this reporting period, the schedule management score is being affected by a late critical path and subtasks showing positive finish variance.  
 Tasks with a positive finish variance are scheduled to finish later than originally planned. At this time, this is not affecting the project's overall end date.

**COST MANAGEMENT** **100%**  
 Cost Management presents low risk.  
 The project was \$95,121 over budget (7%) for the reporting period.  
 The project was \$4,198,681 under budget (30%) for the fiscal year to date.  
 This variance currently does not appear to indicate a negative impact to scope or schedule.

**RISKS & ISSUES MGMT** **100%**  
 Risk & Issue Management presents low risk.  
 There were 33 active risks during the reporting period, including two new risks. There were no closed risks. There was one active risk listed as High Probability / High Impact.  
 There was three active issues during the reporting period. There were no new issues or closed issues.

**PROJECT MGMT PRACTICES** **100%**  
 Project Management Practices present low risk.  
 The project appears to be utilizing sound project management processes.

AGENCY: Department of Financial Services

November 2021



PROJECT: Florida Planning, Accounting, and Ledger Management (PALM)

--	--	--	--	--

SCOPE MANAGEMENT 100%

(This area is intentionally left blank)

--

SCHEDULE MANAGEMENT 75%

(This area is intentionally left blank)

--

COST MANAGEMENT 100%

(This area is intentionally left blank)

--

RISKS & ISSUES MANAGEMENT 100%

(This area is intentionally left blank)

--

PM PRACTICES 100%

(This area is intentionally left blank)

--
